



11/24/2025 – 11/28/2025

# ***WEEKLY UPDATE***

**Project Name:** Creciente Condo

**Client:** Duncan Heath, Wright Construction

**Project Address:** 7150 Estero Blvd, Fort Myers Beach, FL 33931



# WEEKLY TASKS COMPLETED


Day

Overview

Photo Reference

**Monday**  
**11/24/2025**

- Flooded the court
- Started to grind down lines
- Set resurfacer on half the court

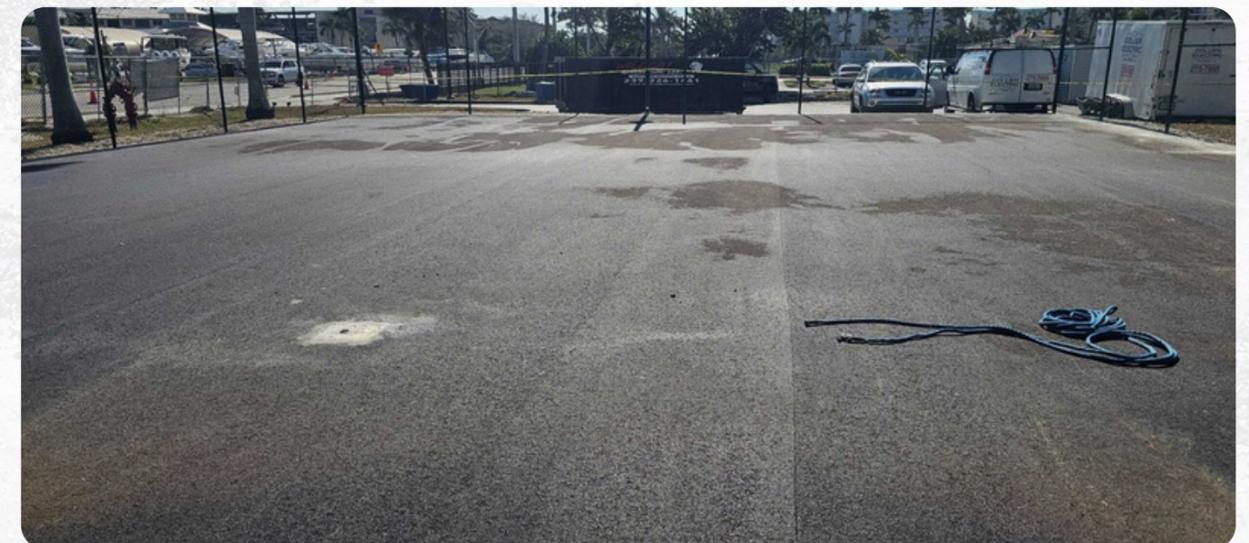

# WEEKLY TASKS COMPLETED


Day

Overview

Photo Reference

**Tuesday**  
**11/25/2025**

- Set both layers of green

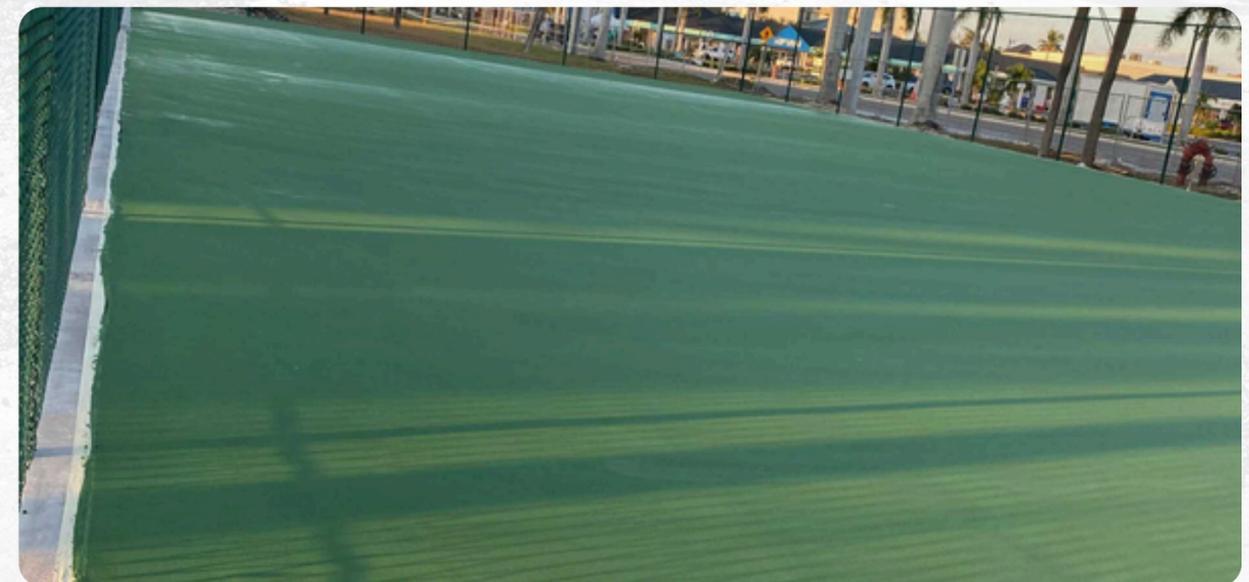

# WEEKLY TASKS COMPLETED

Day

Overview

Photo Reference

**Wednesday**  
**11/26/2025**

- Finished the green
- Set lines and 2 extra PB lines on swiss red

